

D O	Tas	sk Name	Duration	Start	Finish	Predecessors	% Complete	08	15	22	A 29
1	_	E Academic Project	237 days	Sat 14-07-18	Wed 05-06-19		31%	- 00	.0		
2		Phase 1: 7th Semester Activities	100 days	Sat 14-07-18	Mon 26-11-18		86%				
3 🗸		Project Startup	67 days	Sat 14-07-18	Sun 14-10-18		100%				
4 🗸		Team Building	7 days	Sat 14-07-18	Tue 24-07-18		100%				
5 🗸		Brainstorm on Project Topic	7 days	Mon 23-07-18	Tue 31-07-18	4	100%		(
6 🗸		Project agreed with Guide	1 day	Wed 01-08-18	Wed 01-08-18	5	100%				
7 🗸		Related Study & Documentation	15 days	Mon 23-07-18	Fri 10-08-18	4	100%		L		
8 🗸		Deliver Project Synopsis for Guide's review	0 days	Sun 12-08-18	Sun 12-08-18	7	100%				
9 🗸		Close review feedbacks	5 days	Mon 01-10-18	Fri 05-10-18	8	100%				
10 🗸		Project Synopsis Finalized	7 days	Sat 06-10-18	Sun 14-10-18	9	100%				
11 🗸		Requirement Analysis	11 days	Mon 15-10-18	Sat 27-10-18	3	100%				
12 🗸		Gather Requirements	2 days	Mon 15-10-18	Tue 16-10-18		100%				
13 🗸		Prepare Draft Requirement Matrix	0 days	Tue 16-10-18	Tue 16-10-18	12	100%				
14 🗸		Elaborate Rqmt & Document	4 days	Wed 17-10-18	Mon 22-10-18	13	100%				
15		Customer	1 day	Mon 22-10-18	Mon 22-10-18		100%				
16 🗸		Admin	1 day	Wed 17-10-18	Wed 17-10-18		100%				
17 🗸		Coordinator	1 day	Wed 17-10-18	Wed 17-10-18		100%				
18 🗸		Úpdate Requirement Matrix	1 day	Tue 23-10-18	Tue 23-10-18	14	100%				
19		Requirement Matrix Finalized	4 days	Wed 24-10-18	Sat 27-10-18	18	100%				
20		Design	15 days	Fri 02-11-18	Thu 22-11-18		50%				
21 🗸		Detailed Design	12 days	Fri 02-11-18	Mon 19-11-18		100%				
22 🗸		Customer	4 days	Fri 02-11-18	Wed 07-11-18		100%				
23 🗸		Admin	4 days	Thu 08-11-18	Tue 13-11-18		100%				
24 🗸		Coordinator	3 days	Thu 15-11-18	Mon 19-11-18		100%				
25		Test Plan Preparation	11 days	Thu 08-11-18	Thu 22-11-18		0%				
26		Customer	-	Thu 08-11-18	Tue 13-11-18	22	0%				
27		Admin	4 days				0%				
	1		4 days	Wed 14-11-18	Mon 19-11-18	23					
28 1		Coordinator	3 days	Tue 20-11-18	Thu 22-11-18	24	0%				
29 🗸		Phase 1 Closure	5 days	Tue 20-11-18	Mon 26-11-18	20	100%				
30 🗸		Prepare 7th Semester Project Report	4 days	Tue 20-11-18	Fri 23-11-18		100%				
31 🗸		Updated Requirement Matrix	0 days	Sun 25-11-18	Sun 25-11-18	30	100%				
32 🗸		Updated Project Plan	0 days	Sun 25-11-18	Sun 25-11-18	31	100%				
33 🗸		Project Viva	1 day	Mon 26-11-18	Mon 26-11-18	32	100%				
34 🗸		Approved Project Report - 7th Semester	0 days	Mon 26-11-18	Mon 26-11-18	33	100%				
35	١.	Semester Gap	32 days	Tue 27-11-18	Wed 09-01-19	2	0%				
36		Phase 2: 8th Semester Activities	105 days	Thu 10-01-19	Wed 05-06-19	35	0%				
37		Coding & Únit Testing	80 days	Thu 10-01-19	Wed 01-05-19		0%		 		
		Task		Rolled Up Task		External	Tasks				
Projec	t CS	SE Project Progress		Rolled Up Miles	tone ♦	Project S	Summary				
		29-11-18 Milestone •		Rolled Up Progr		-	y Summary				
		Summary		Split				₩			

ID]	Task Name	Duration	Start	Finish	Predecessors	% Complete				Aug
						·	08	15	22	29
38	TBD	80 days	Thu 10-01-19	Wed 01-05-19		0%				
39	System Integration Testing	10 days	Thu 02-05-19	Wed 15-05-19	37	0%				
40	TBD	10 days	Thu 02-05-19	Wed 15-05-19		0%				
41	Project Closure	15 days	Thu 16-05-19	Wed 05-06-19	39	0%				
42	Prepare 8th Semester Project Report	14 days	Thu 16-05-19	Tue 04-06-19		0%				
43	Updated Requirement Matrix	0 days	Tue 04-06-19	Tue 04-06-19	42	0%				
44	Updated Project Plan	0 days	Tue 04-06-19	Tue 04-06-19	43	0%				
45	Review by Faculties	1 day	Wed 05-06-19	Wed 05-06-19	44	0%				
46	Approved Project Report - 7th Semester	0 days	Wed 05-06-19	Wed 05-06-19	45	0%				



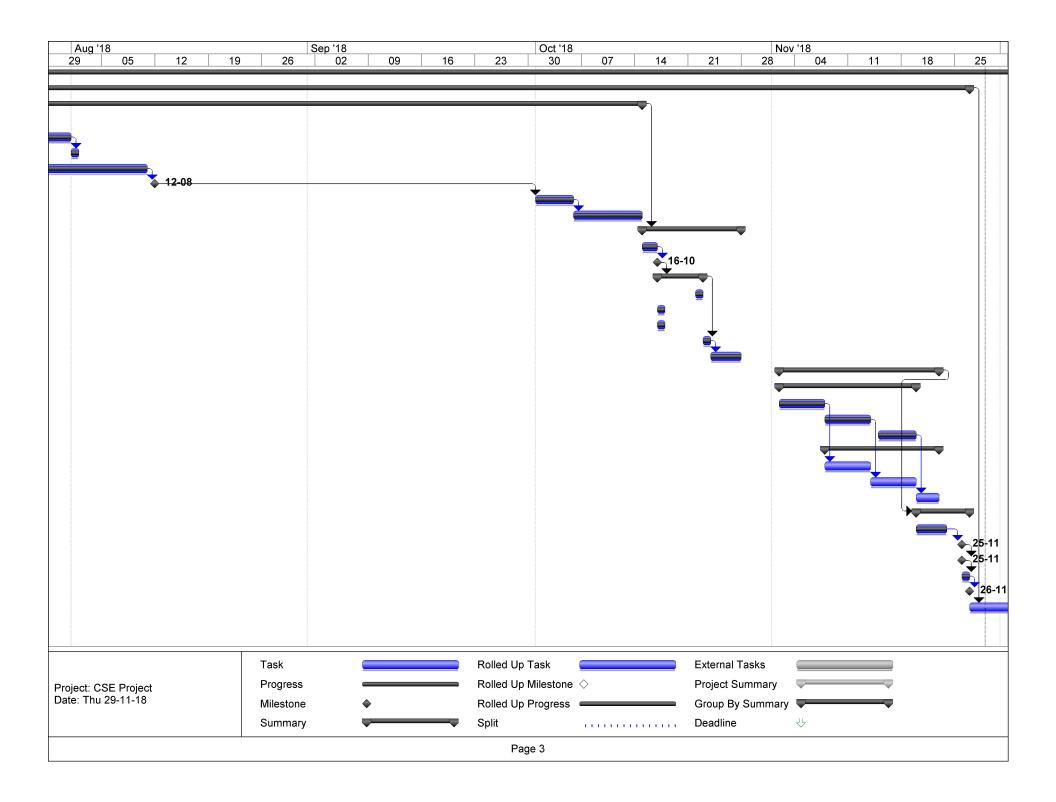

Aug '18 29	05		12	19		26	Sep	'18 02		09	16		23		Oct '18 30	3	07	14		21		N 28	lov '1	8 04	11		18	25
	05		12	19		20		02		09	10				30		07	14		Z I				04	11		10	25
													. 11		1													
					Task								olled L							xterna						ļ		
Project: CSI Date: Thu 2	E Projec	t			Prog	ress					\longrightarrow	R	olled L	Jp Mi	leston	>			Р	roject	Sumi	mary				7		
Date: Thu 2	9-11-18				Miles	stone			\rightarrow			R	olled L	Jp Pr	ogress				G	roup I	By Su	ımmaı	ry 🛡		_	,		
						mary			_				olit					 		eadlin			₩.					
													F	⊃age	4													
