ID		Task Name	Duration	Start	Finish	Predecessors	% Complete	Resource Names	Notes
1		**CSE Academic Project**	**258 days**	**Sat 14-07-18**	**Thu 04-07-19**		**17%**		
2		**Phase 1: 7th Semester Activities**	**121 days**	**Sat 14-07-18**	**Tue 25-12-18**		**30%**		
3	✓	**Project Startup**	**67 days**	**Sat 14-07-18**	**Sun 14-10-18**		**100%**		
4	✓	Team Building	7 days	Sat 14-07-18	Tue 24-07-18		100%		
5	✓	Brainstorm on Project Topic	7 days	Mon 23-07-18	Tue 31-07-18	4	100%		
6	✓	Project agreed with Guide	1 day	Wed 01-08-18	Wed 01-08-18	5	100%		
7	✓	Related Study & Documentation	15 days	Mon 23-07-18	Fri 10-08-18	4	100%		
8	✓	Deliver Project Synopsis for Guide's review	0 days	Sun 12-08-18	Sun 12-08-18	7	100%		
9	✓	Close review feedbacks	5 days	Mon 01-10-18	Fri 05-10-18	8	100%		
10	✓	**Project Synopsis Finalized**	**7 days**	**Sat 06-10-18**	**Sun 14-10-18**	**9**	100%		
11	✓	**Requirement Analysis**	**11 days**	**Mon 15-10-18**	**Sat 27-10-18**	**3**	**100%**		
12	✓	Gather Requirements	2 days	Mon 15-10-18	Tue 16-10-18		100%		
13	✓	Prepare Draft Requirement Matrix	0 days	Tue 16-10-18	Tue 16-10-18	12	100%		
14	✓	**Elaborate Rqmt & Document**	**4 days**	**Wed 17-10-18**	**Mon 22-10-18**	**13**	**100%**		
15	✓	Customer	1 day	Mon 22-10-18	Mon 22-10-18		100%		
16	✓	Admin	1 day	Wed 17-10-18	Wed 17-10-18		100%		
17	✓	Coordinator	1 day	Wed 17-10-18	Wed 17-10-18		100%		
18	✓	Úpdate Requirement Matrix	1 day	Tue 23-10-18	Tue 23-10-18	14	100%		
19	✓	**Requirement Matrix Finalized**	**4 days**	**Wed 24-10-18**	**Sat 27-10-18**	**18**	100%		
20		**Design**	**34 days**	**Thu 18-10-18**	**Fri 30-11-18**		**0%**		
37		**Phase 1 Closure**	**17 days**	**Mon 03-12-18**	**Tue 25-12-18**	**20**	**0%**		
43		**Semester Gap**	**32 days**	**Wed 26-12-18**	**Thu 07-02-19**	**2**	0%		Some of the dates ar
44		**Phase 2: 8th Semester Activities**	**105 days**	**Fri 08-02-19**	**Thu 04-07-19**	**43**	**0%**		
45		**Coding & Únit Testing**	**80 days**	**Fri 08-02-19**	**Thu 30-05-19**		**0%**		
47		**System Integration Testing**	**10 days**	**Fri 31-05-19**	**Thu 13-06-19**	**45**	**0%**		
49		**Project Closure**	**15 days**	**Fri 14-06-19**	**Thu 04-07-19**	**47**	**0%**		



Project: CSE Project
Date: Mon 29-10-18

Task		Rolled Up Task		External Tasks	
Progress		Rolled Up Milestone		Project Summary	
Milestone		Rolled Up Progress		Group By Summary	
Summary		Split		Deadline	

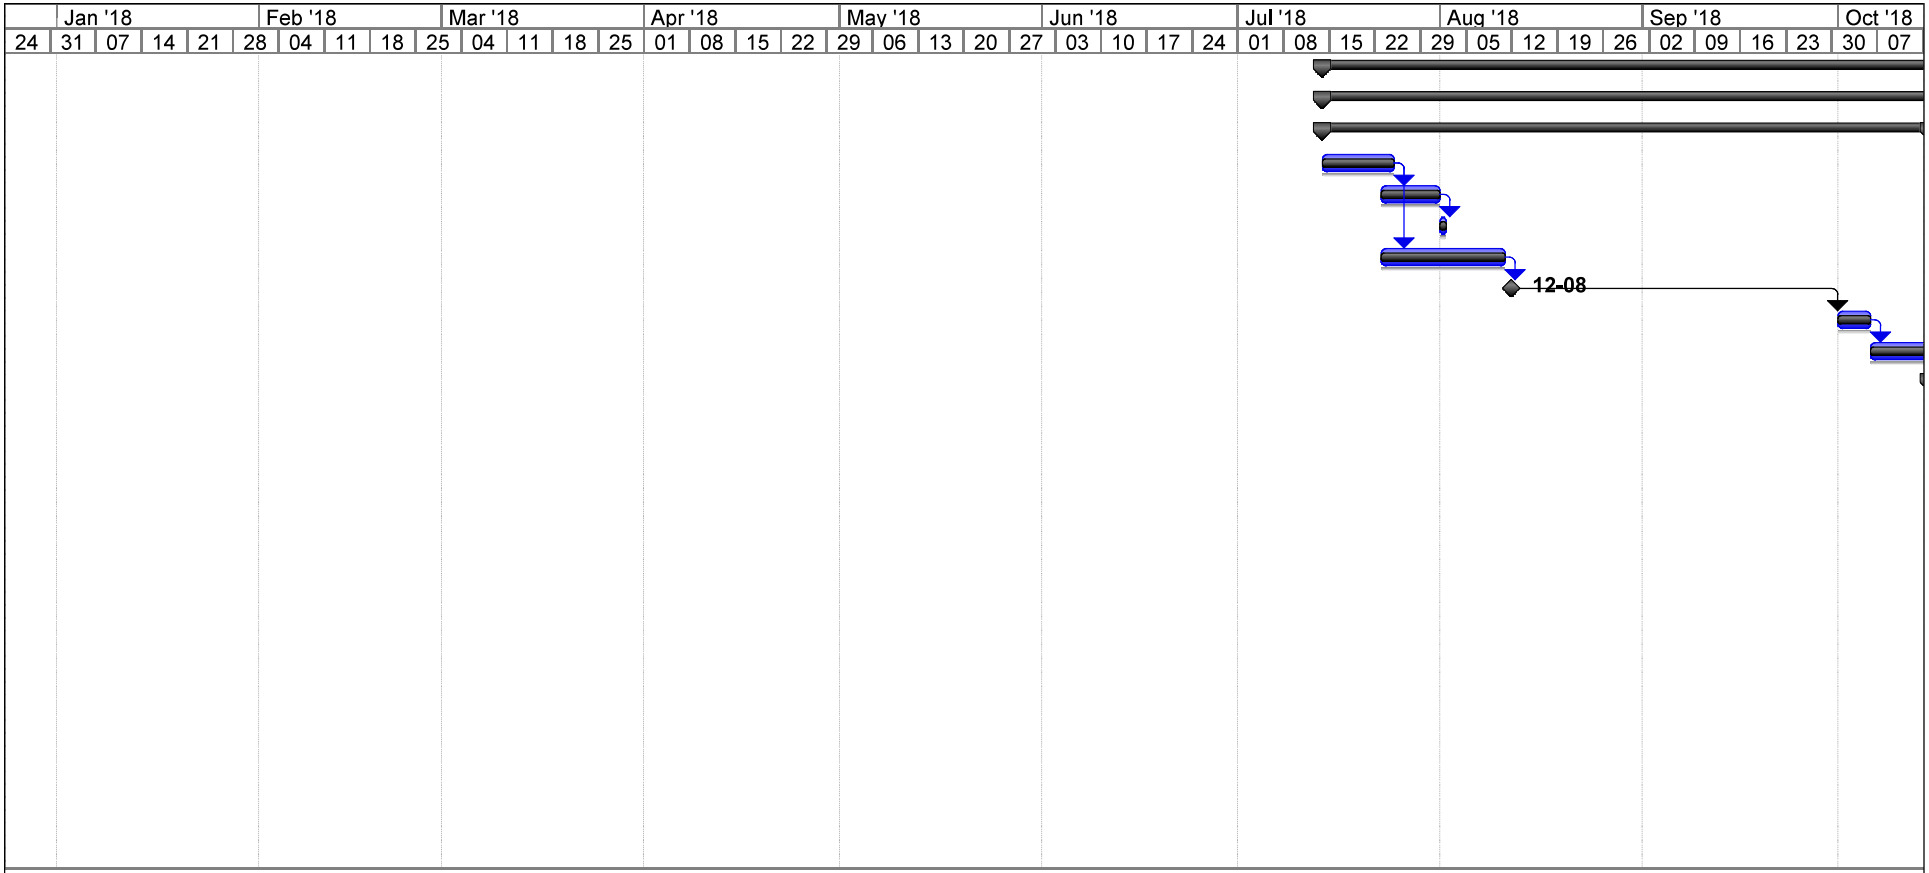

Project: CSE Project
Date: Mon 29-10-18

Task		Rolled Up Task		External Tasks	
Progress		Rolled Up Milestone	◇	Project Summary	
Milestone	◆	Rolled Up Progress		Group By Summary	
Summary		Split		Deadline	⇩

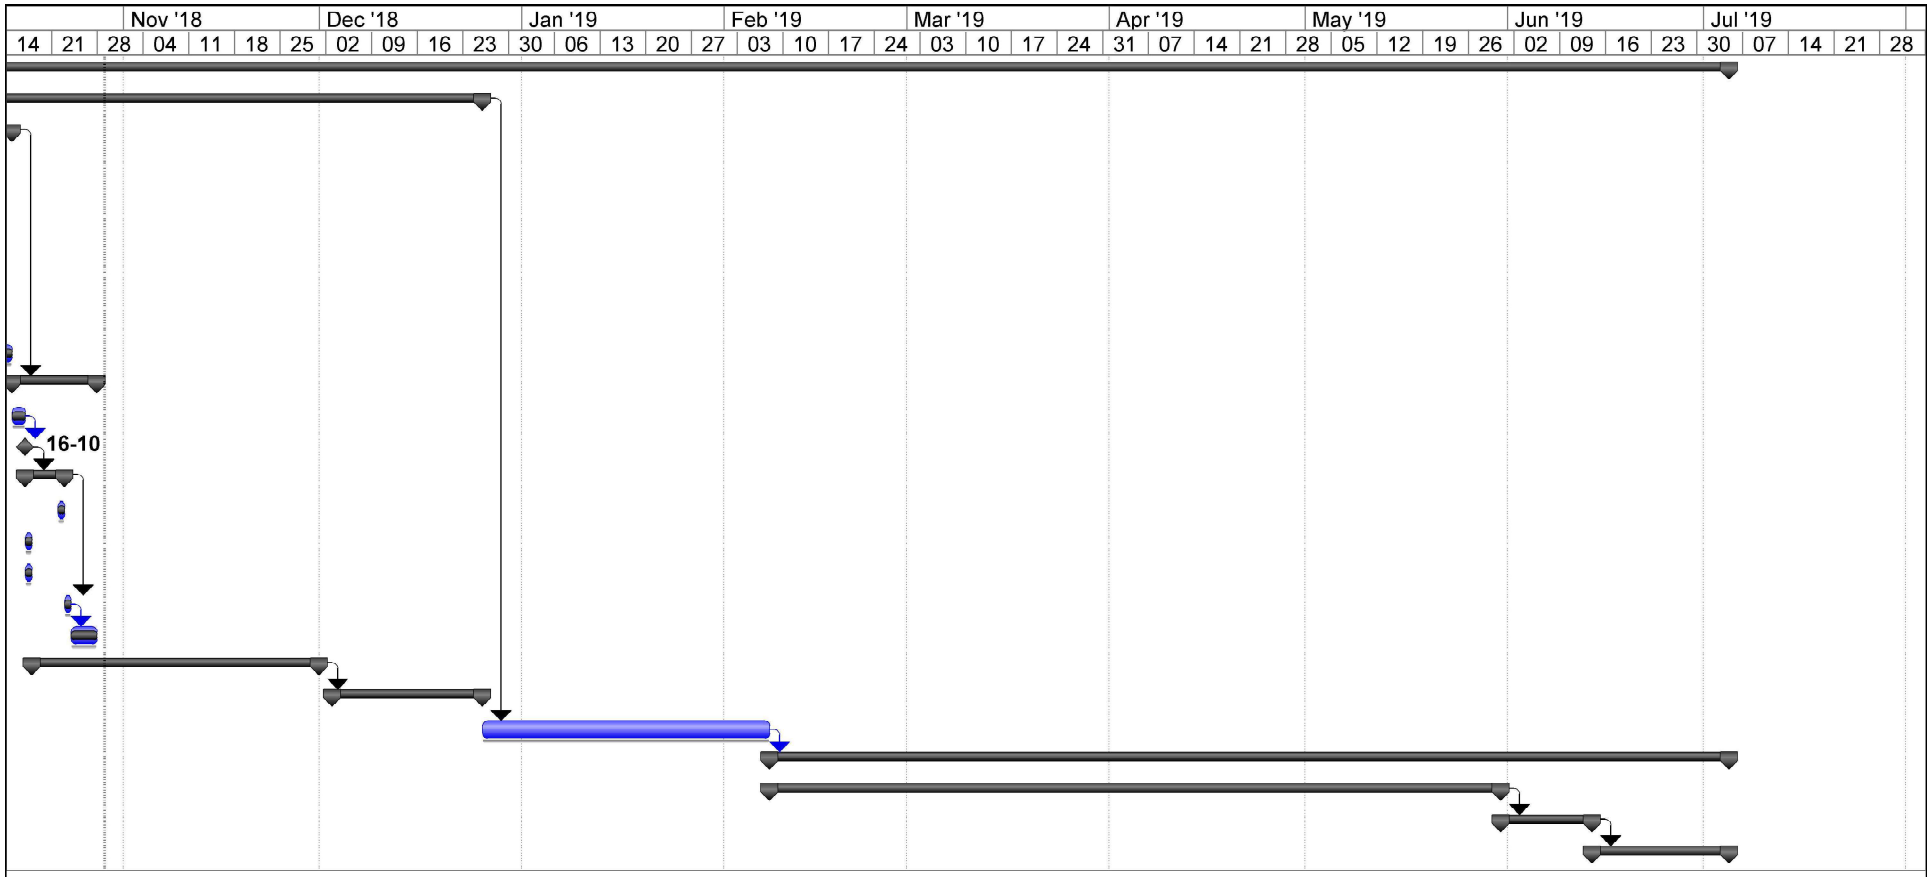

Project: CSE Project
Date: Mon 29-10-18

Task		Rolled Up Task		External Tasks	
Progress		Rolled Up Milestone	◇	Project Summary	
Milestone	◆	Rolled Up Progress		Group By Summary	
Summary		Split		Deadline	⇩
